

NOTES ON MODULARITY FOR MMC

The building has been designed to allow for a modular approach to large parts of the construction. The viability of this method of construction is to be determined by a competitive tender process. Contractors are invited to leverage Modern Methods of Construction (MMC) to deliver the building. The following design approach has been developed to allow for innovative, high quality, cost effective outcomes, pending market availability and expertise. A traditionally documented building with key MMC characteristics has been provided as a benchmark.

MMC PROCUREMENT

Any MMC submissions must allow for shop drawing processes and review against the design outcomes and qualities documented for the traditional procurement option. In addition the cost for this work and additional certification and design work (e.g. seismic services design for MMC, additional footings/sub floor structure etc. is to be borne by the tenderer/contractor).

THE MODULE

A module of 12.6m long x 4.2m wide has been used to develop the plan. This module allows for transportation within reasonable limitations. The module has a 3:1 ratio allowing for logical assembly.

THE PLAN

The plan of the building has been conceived of as 32 modules arranged in a square donut shape, creating an inner courtyard. The square comprises two horizontal arrays of 11 modules connected by two vertical arrays of five modules.

MODULARITY IN SECTION


The module is conceived to encapsulate the floor subframe and the ceiling subframe. With a typical ceiling height of 3m it is anticipated that this provides a module of approximately 3.3m to 3.4m in height. To allow for a rational roofing structure and drainage strategy the roof is thought to be installed in-situ on top of the modular ceiling. The feature facade cladding would also be installed on site along with the internal courtyard deck and awning.

WALL SETOUT LOGIC


The logic for the wall setout is true to the modular strategy for the building, with the walls predominantly setout with a face to the grid line (not centred on grids). Some walls are within a module where planning and efficiency requires it. As the building is being traditionally documented, the structure is rationalised for a traditional construction methodology and some redesign for a modular method is expected. The planning should be maintained unless adjustments are absolutely necessary to allow for a modular approach.

SUB FLOOR STRUCTURE


If an MMC approach is selected additional / amended footings and sub floor structure will need to be considered, documented and approvals for changes sought as part of the tender process.

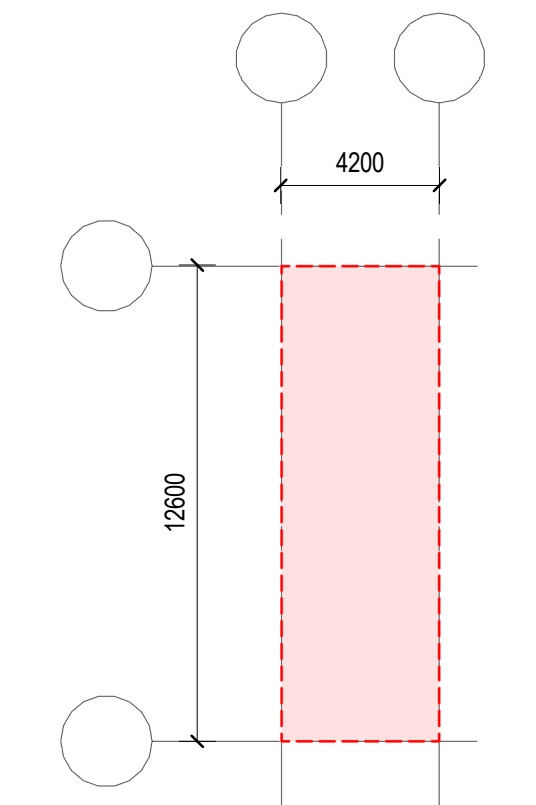


27 Module Dimensions  
1 : 200  
Nominally 32 in number

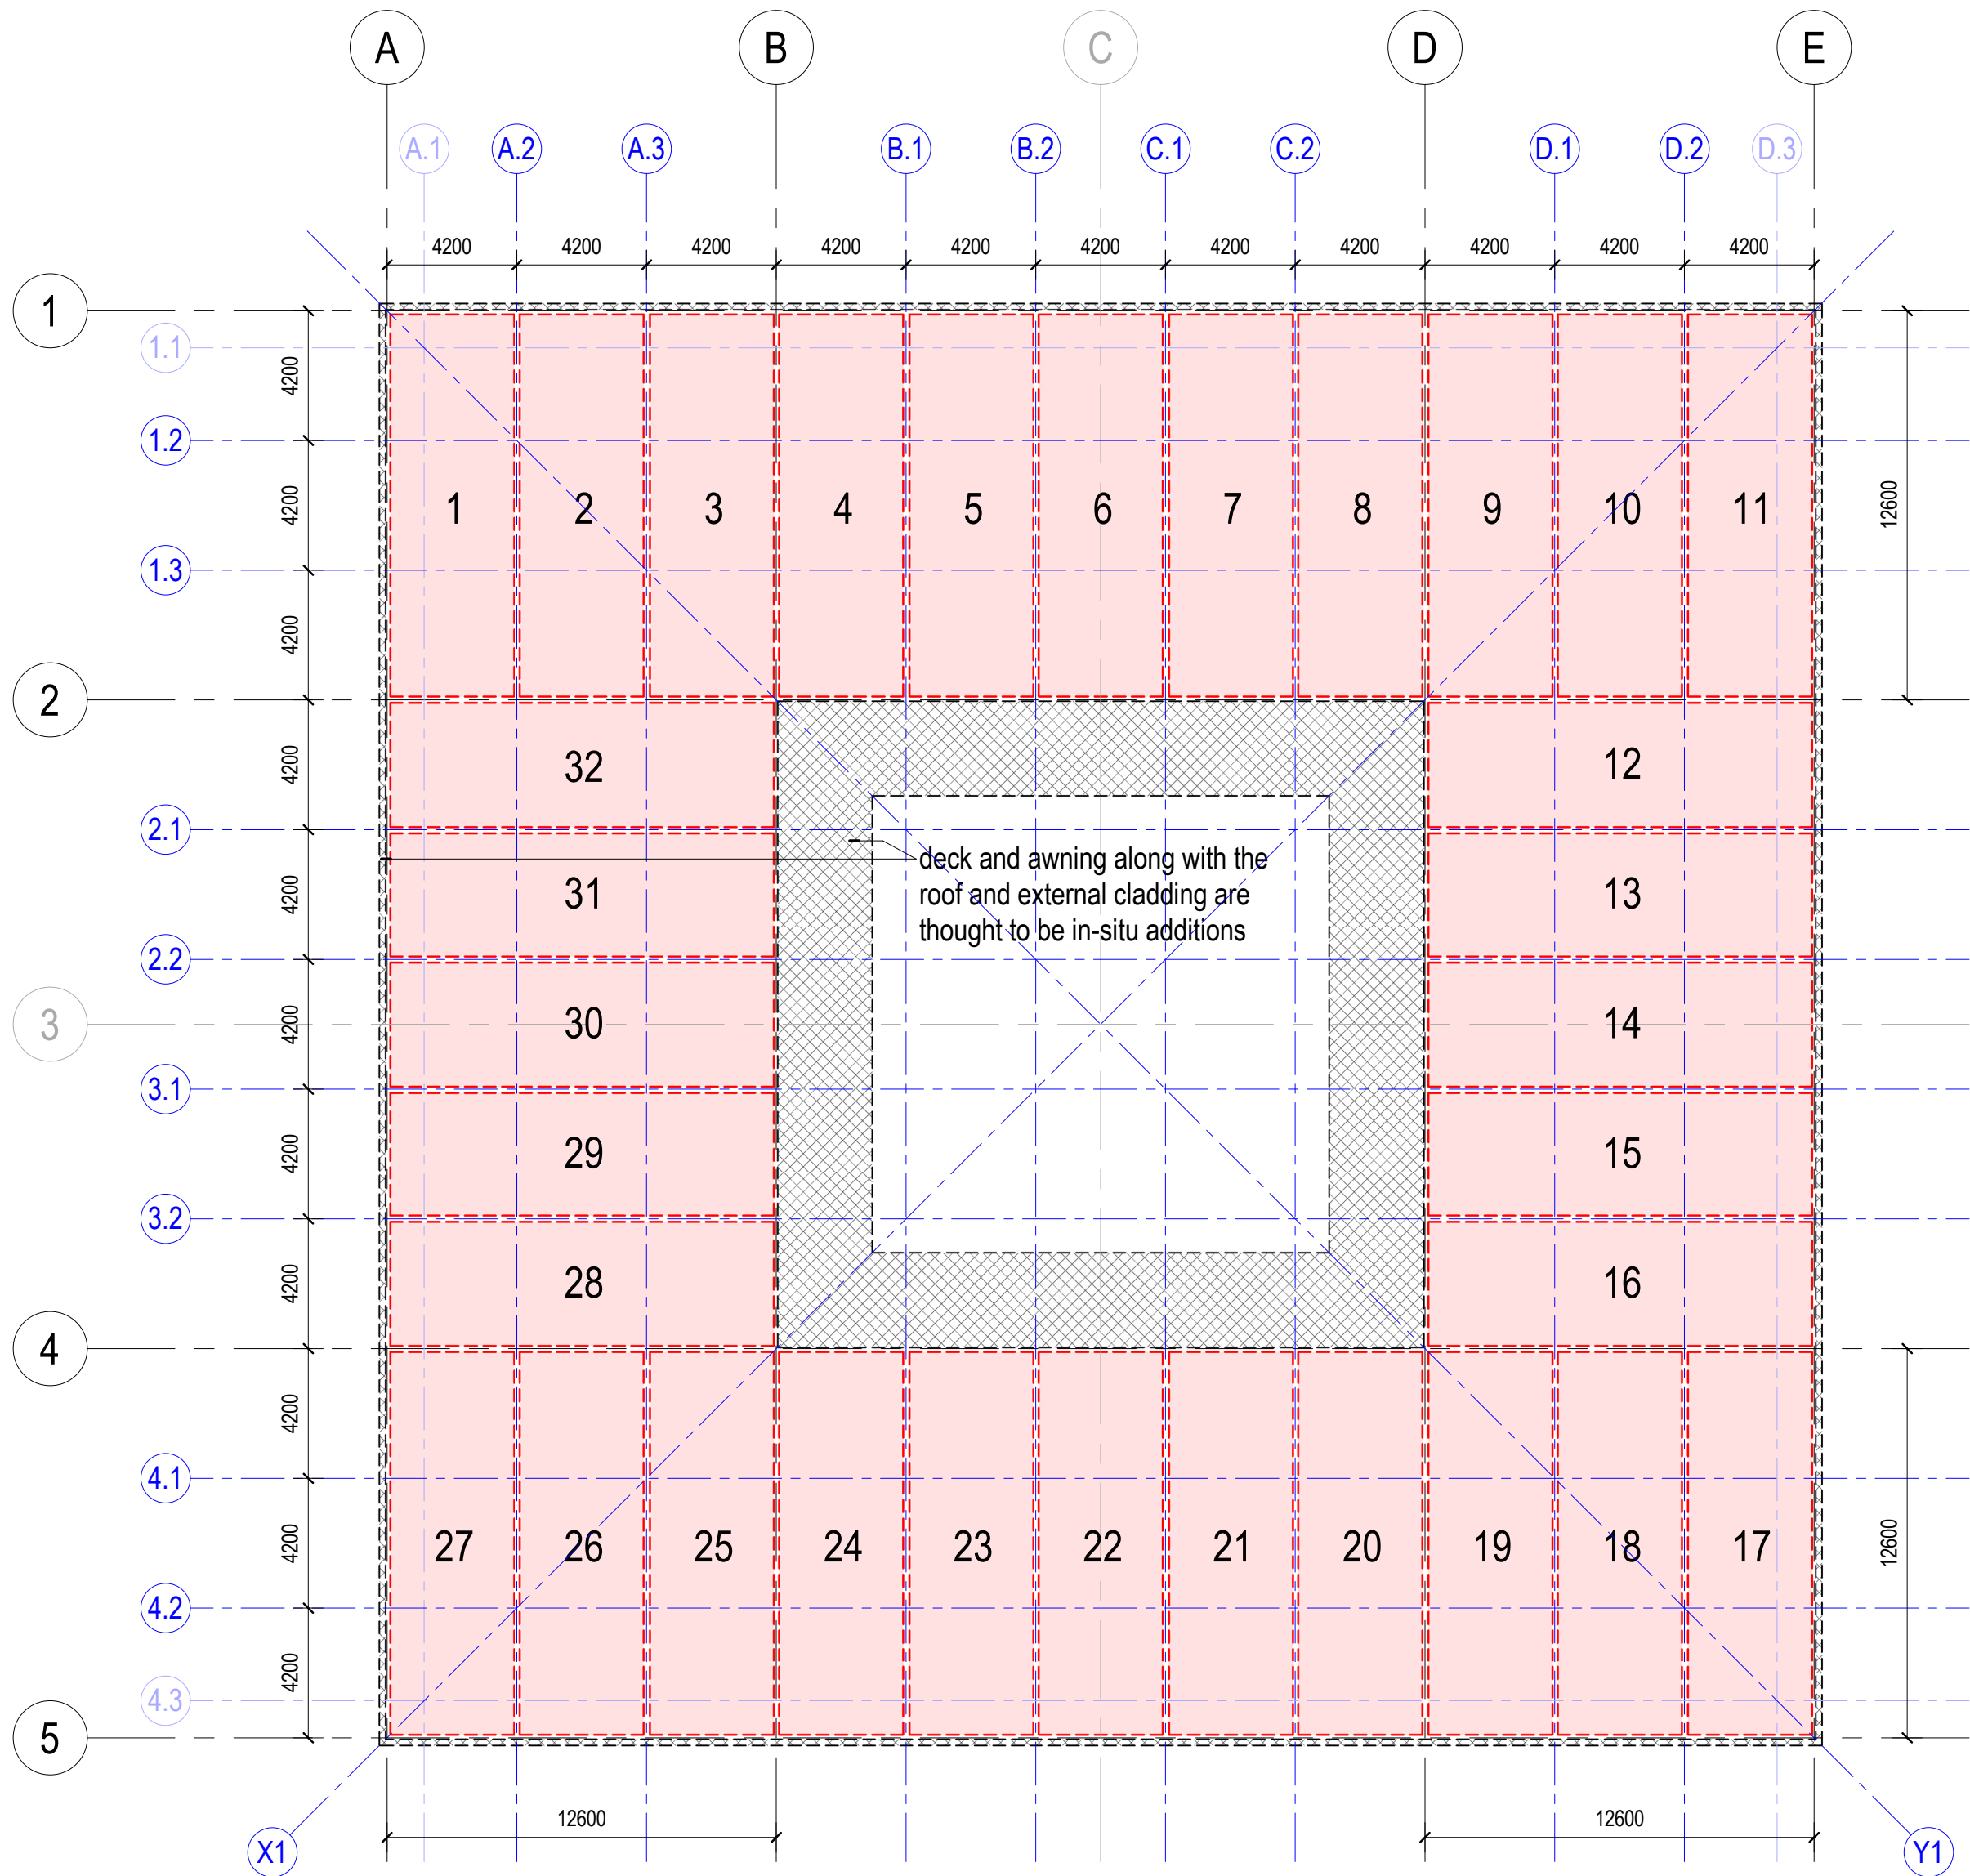

32 Overall Modular Strategy - Plan  
1 : 200  
NOTE: refer to detailed plans for meeting room / infill, external spaces, external works, floor / roof penetrations, drainage, etc.

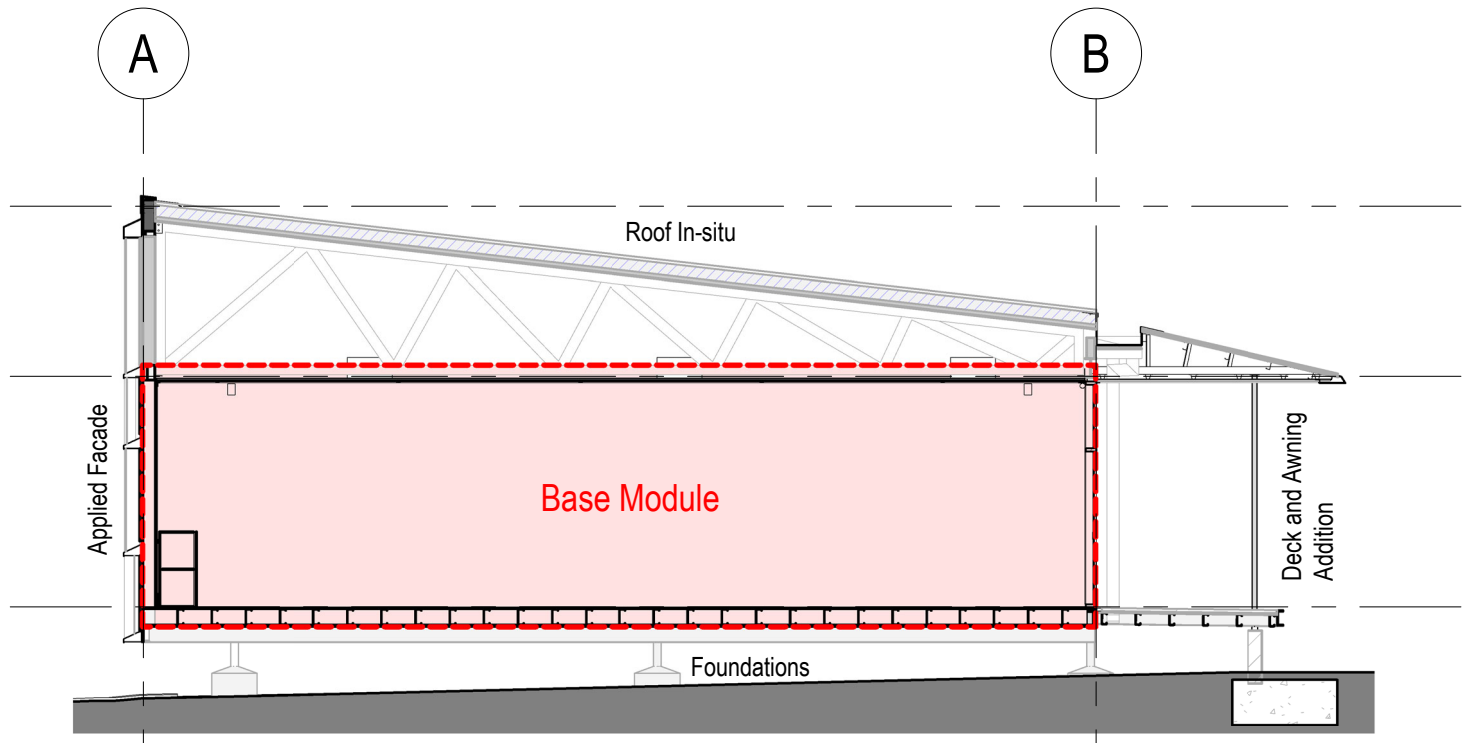

33 Modularity in Section  
1 : 100

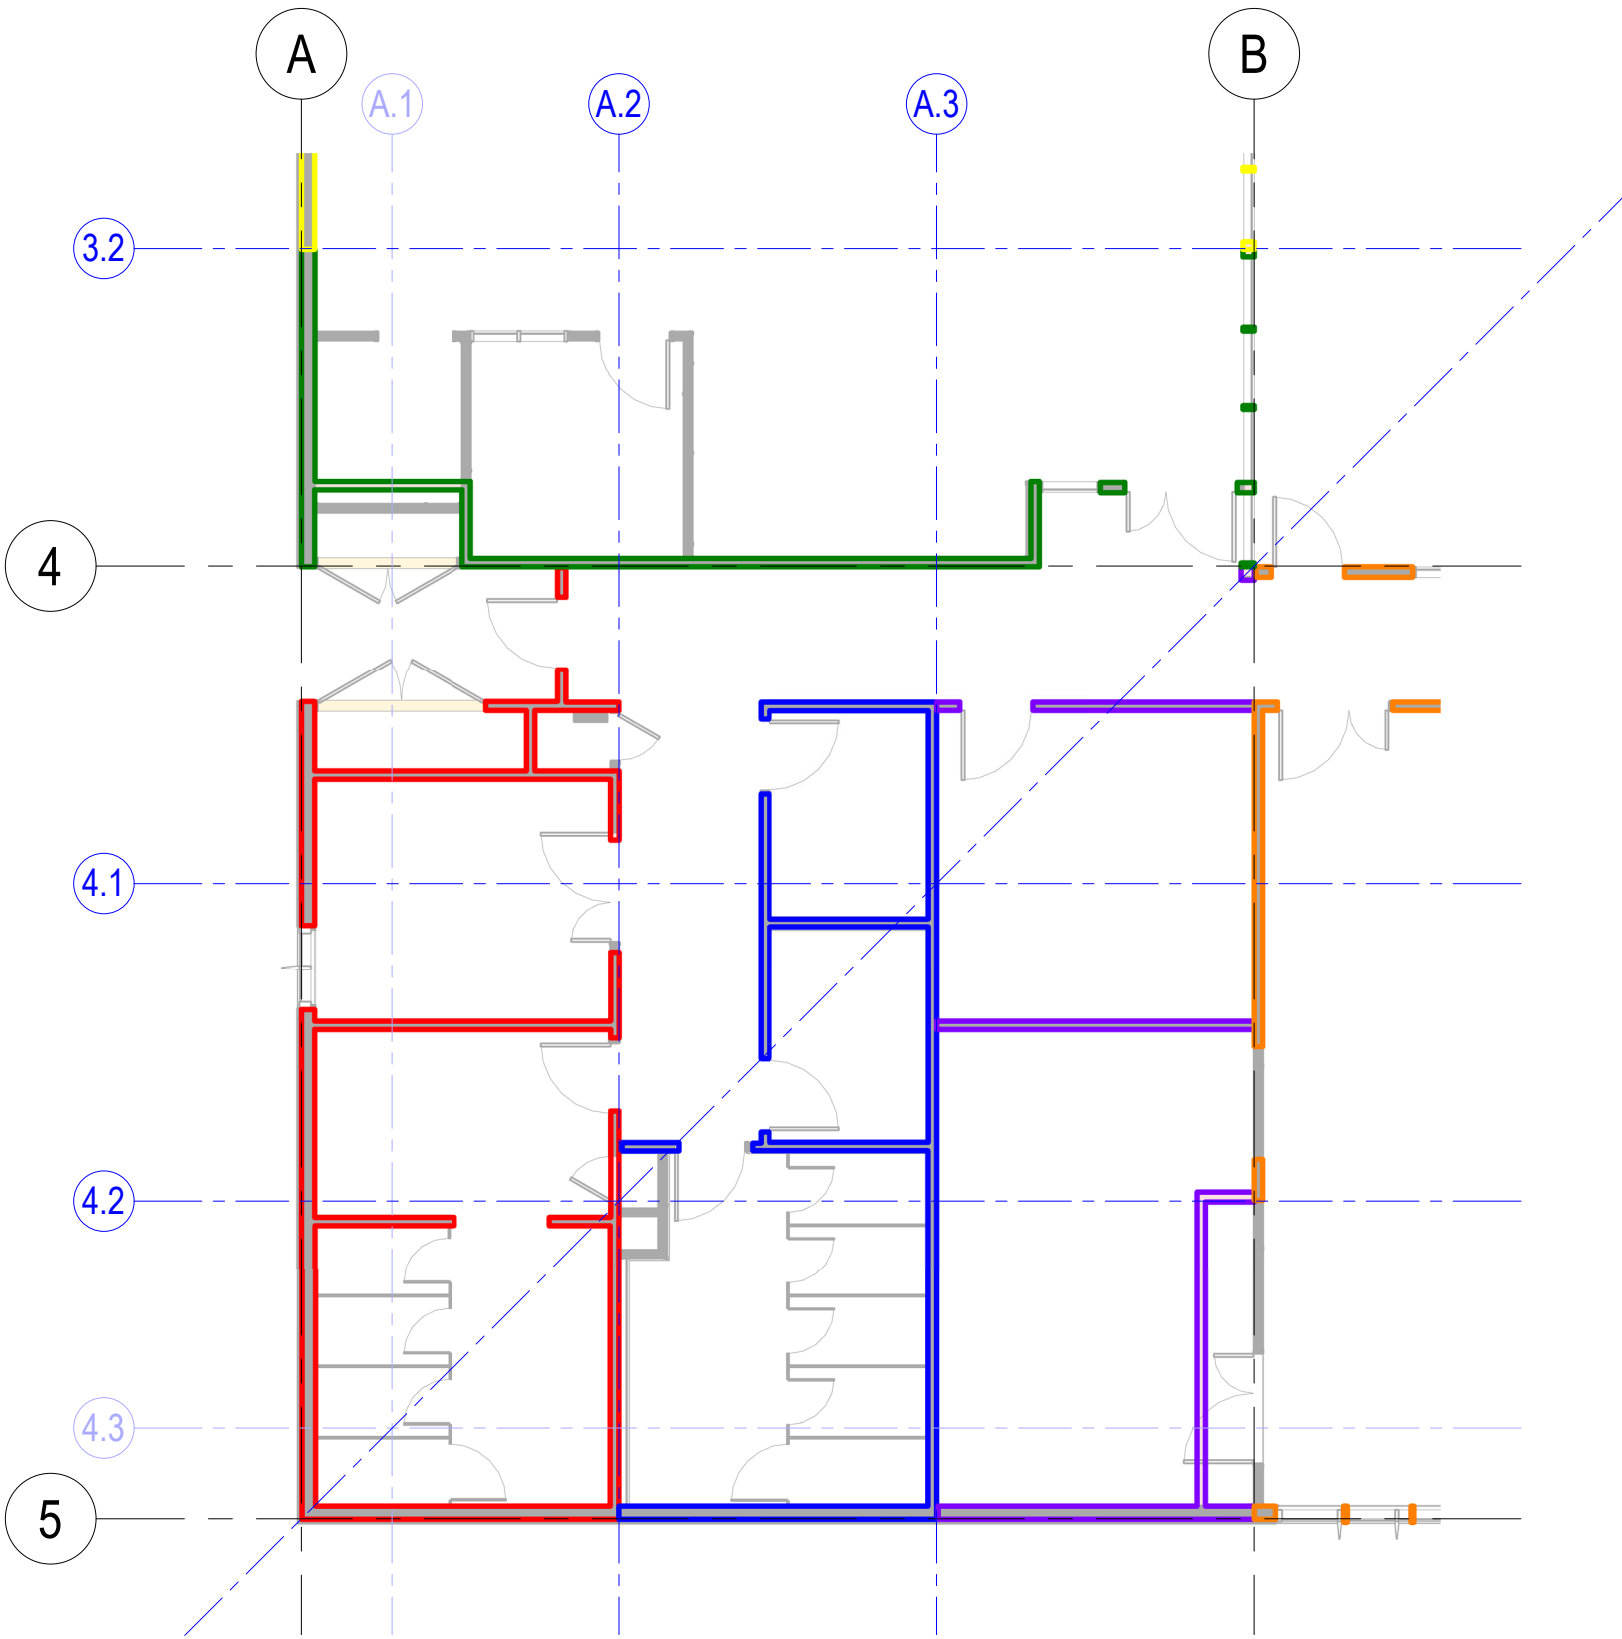

35 Wall Setout Logic  
1 : 100

PRELIMINARY  
NOT FOR CONSTRUCTION

Drawings include colour information. A black & white copy may not have all the information. This background is coloured blue.

brian hooperarchitect  
m3architecture  
ph: +61 7 3831 4644  
11 saint james street petrie tce q 4000  
info@m3architecture.com  
www.m3architecture.com

client  
stanwell

project  
Stanwell New Projects Office  
Switchyard Road,  
Stanwell, QLD, 4702

title  
Design Development Notes

drawn bg  
checked jb  
date March 2026  
scale As indicated at A1  
drawing 25010 / cd A-910001 / T1

copyright ©  
These designs, plans, specifications and the copyright herein are the property of the architect and must not be used, reproduced, or copied wholly or in part without the written permission of m3architecture Pty Ltd abn 23 079 044 545. Use figured dimensions in preference to scale. If there are any questions contact the architect.

1:1 at A1  
0 10 20 30 40 50mm
